

A2530 28.12.18

PATIL INDUSTRIAL EQUIPMENT COMPANY
FORM NO 11

(See rules 62 and 64) Ref No- P/22/2018 / RI / 1073
Report of examination of Hoist, Lift, Lifting machines, chains ropes and Lifting Tackles.

		PARTICULARS
1.	Name of occupier	: ABB India Ltd
2.	Name & address of factory	: EPMV Gas Insulated Switchgear, Plot No 34, M I D C Satpur, Nasik 422007
3.A	Type, identification number and description of hoist lift, lifting machine chains, ropes, and lifting tackles	: Column Mounted Jib Crane : With Stahl make Chain Hoist Sr. No 3127114 : Capacity 500 Kg. 1 Fall Chain Dai 05 MM : Location: Loading & Unloading Area HOL- 3.8 MTR : 2017-18 : 03 / 03 / 2018
	Date of construction or reconstruction and the date when the hoist , lift, lift machine, chains, ropes, and Lifting tackles were first taken into use in the factory.	
4	Date of last examination made under section 28	: 03 / 03 / 2018 First Exam
(1)	(a) (ii) and 29 (1) (a) (iii) and by whom it was carried out	: S G Patil C P C No P/22/2017
5(A)	Maintenance (list of parts , if any which were Inaccessible)	: N.A
	Are the following parts of the hoist or lift properly Maintained and in good working order? If not state what defects have been found.	
(a)	Enclosure of hoist way or lift way	: N.A.
(b)	Landing gates and cage gate (s)	: N.A.
(c)	Interlocks on the landing gates and cage gate (s)	: N.A.
(d)	Other gates fastenings.	: N.A.
(e)	Cage and platform and fitting cage guides buffers , interior of the hoist way or lift way	: N.A.
(f)	OVERRUNNING devices.	: N.A.
(g)	Suspension ropes or chains and their attachment.	: N.A.
(h)	Safety gear, i.e arrangements for preventing fall of platform or cage brakes.	: N.A.
(i)	Brakes.	: N.A.
(j)	Worm or spur gearing	: N.A.
(k)	Other electrical equipment.	: N.A.
(l)	Other parts	: N.A.
5(B)	Date and number of the certificate relating to any test and examination made under sub rule (1) of rule 64 together with the name of the person who issued the certificate.	: 03 / 03 / 2018 First Exam : S G Patil C P C No P/22/2018
5(C)(i)	Date of annealing or the heat treatment of the Chain and lifting tackle carried out under sub rule (5) of rule 64 and by whom it was carried out.	: N.A.
(ii)	Particulars of any defect at any such examination or after annealing and affecting the safe working Load and of the steps taken to remedy such defect.	: Nil
6	Repairs renewals or alterations (if any) required and the period within which they should be executed and Maximum safe working load subject to repairs , renewals Or alterations (if any)	: Nil . Visually examined, Loads Tested, Found no defect affecting Safe working Load.

I/We certify that on 03 / 03 / 2018 I/We thoroughly examined the hoist , lift and lifting machine , ropes and lifting tackles & details of examination/ test carried out are enclosed herewith and that the above is a correct report of the result.

Signature

Name- S.G. PATIL.

Qualification :- B.E. (Mech) D.E.E , M.I.E,

COMPETENT PERSON

C.P.C NO- P/22/2018

CHARTERED ENGINEER. M061452-6

Counter signature

If employed by a company or a Association

PATIL IND EQUIP COMPANY

Flat no- A-2, Suvarnyug Coop Hsg Soc.


New D. P. Road, Aundh, Pune- 411007

Phone- 020-25886155

Mob- 94220-88626

Date- : 03 / 03 / 2018

Next testing Due Date : 02 / 03 / 2019

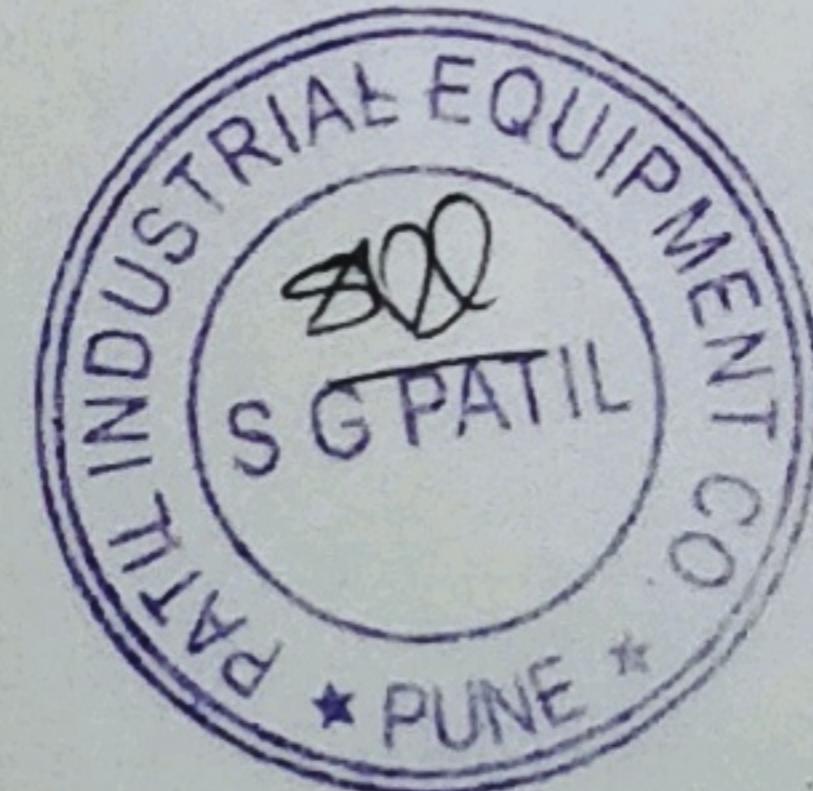



SPARKLINE EQUIPMENTS PVT. LTD.
PLOT NO-38, F-II BLOCK, MIDC, PIMPRI, PUNE
E-MAIL : aftersales.pune@sparkline.co.in
SERVICE TOLL FREE NUMBER: 18002661677



INSTALLATION & COMMISSIONING REPORT

CUSTOMER NAME	ABB India Ltd	
CUSTOMER ADDRESS	PPMV-outdoorCKTBreaker, nashik	
	DMS-Medium voltage switchgear	
	Plot No.79, street no.17	
MIDC industrial area Satpur Nashik 422007		
Purchase Order No.	3091029444	PO Date: 16/11/2017
PROJECT CODE	A25J028_1718 & A25I107_1718	
EQUIPMENTS DETAILS	Location..... : Loading & Unloading Area	
	Type of Equipment..... : Column Mounted Jib Crane With Hois	
	Equipment Number..... : ST 1005 8/2 1/1	
	Hoist Serial Number..... : 3127114	
	Capacity of the system..... : 500 KG	
	Cross Travel [CT]..... 5.5 MTR	
	Long Travel [LT]..... : NA	
Height Of Lift [HOL]..... : 3.8 MTR		
COMMISSIONING DATE	24/03/2018	
PERSON CONTACTED	Mr. Subhasish Pattnaik	Mobile No: 9765558123
CUSTOMER REMARKS	1) Total taken - bound shay	
	2)	
	3)	
	4)	
	5)	

Equipment Supplied, Installed & Commissioned Working Satisfactorily.

INSTALLED BY

S. Pattnaik
Subhasish Pattnaik

SIGNATURE OF ERECTION ENGINEER
FOR SPARKLINE EQUIPMENTS PVT.LTD.

VERIFIED BY

S. Pattnaik
Subhasish Pattnaik

SIGNATURE OF CUSTOMER



SPARKLINE EQUIPMENTS PVT. LTD.

PLOT NO-38, F-II BLOCK, MIDC, PIMPRI, PUNE
E-MAIL : aftersales.pune@sparkline.co.in
SERVICE TOLL FREE NUMBER: 18002661677



INSTALLATION EVALUATION REPORT

DATE :			
TIME :	NAME OF THE INSTALLATION ENGINEER : sandeep dhawalkar		
CUSTOMER NAME	ABB India Ltd		
PURCHASE ORDER NO	3091029657	PO DATE:	8/12/2017
PROJECT CODE	A25J029-1718 + A25I129-1718		

Arrival at Site	<input checked="" type="checkbox"/>	On-Time	<input type="checkbox"/>	Late	<input type="checkbox"/>	Always Late
Competency Level	<input checked="" type="checkbox"/>	Excellent	<input type="checkbox"/>	Good	<input type="checkbox"/>	Dissatisfied
Follow Safety Rules	<input checked="" type="checkbox"/>	Excellent	<input type="checkbox"/>	Good	<input type="checkbox"/>	Dissatisfied
Workmanship	<input checked="" type="checkbox"/>	Excellent	<input type="checkbox"/>	Good	<input type="checkbox"/>	Dissatisfied
Execution Ability	<input checked="" type="checkbox"/>	Excellent	<input type="checkbox"/>	Good	<input type="checkbox"/>	Dissatisfied
Verbal Communication	<input checked="" type="checkbox"/>	Excellent	<input type="checkbox"/>	Good	<input type="checkbox"/>	Dissatisfied
Overall Experience	<input type="checkbox"/>	Excellent	<input type="checkbox"/>	Good	<input type="checkbox"/>	Dissatisfied

Any comments, questions or suggestions?

[Large empty rectangular box for comments]

Name of Evaluator : Kunal Waknude

Contact Number : 9158677333

E-Mail ID : Kunal.Waknude@in.abb.com

!! We Reassure Our Best Installation & Commissioning For You !!

SIGNATURE OF THE CUSTOMER

sandeep dhawalkar
11/12/2018

SIGNATURE OF INSTALLATION ENGINEER

PATIL INDUSTRIAL EQUIPMENT COMPANY

- Testing of Lifting Machines, Tackles, Pr. Vessels
- Safety Audit Reports • Certificate of Stability
- Industrial safety training to staff and workers

S. G. PATIL B.E. (Mech.); D.E.E., M.I.E.
Chartered Engineer / Competent Person
Valuer (Plant & M/cy.)
Mobile No. : 94220 88626

PUNE OFFICE : BLDG. NO. A, FLAT NO. 2, SUVARNYUG CO-OP. NEAR MEDIPOINT HOSPITAL, NEW D.P. ROAD,
AUNDH, PUNE 411 007. TEL/FAX NO. 25886155. Email : patilindustrialequipmentco@gmail.com

BELGAVI OFFICE : PLOT NO. 80, UDYAMBAG, BELGAVI - 590 008. TEL. : 0831 - 2441691

P/22/2018 / 1072

Date. 14/03/2018

TEST CERTIFICATE OF M.S. STRUCTURE OF COLUMN & ARM

We hereby certify that the below mentioned Structure of Column & Jib Arm Assemblies was Examined as stated below by the Competent Person and found in Satisfactory Condition.

1. Name of Client – : ABB India Ltd
EPMV Gas Insulated Switchgear
Plot No 34, M I D C Satpur, Nasik 422007
2. Description of Structure/ component : M S Structural Material OF Column & Jib Arm Assemblies for JIB CRANE of Capacity 0.5 MT
Drg No FJ 13150003 (R4)
3. Location. : Shop
4. Safe Working Load – : 0.5 MT
5. Proof Load Applied – : 0.75 MT
6. Date of Test – : 03/ 03 /2018
7. Due Date : 02 / 03 /2019
8. Remarks – : Test results found Satisfactory. Refer Drg No FJ 13150003(R4)
Enclosed herewith for more details.

Signature.

Name : S.G.Patil.
Qualification : B.E.(Mech).D.E.E., MIE.
CHARTERED ENGINEER.
COMPETENT PERSON
C.P.C.NO.P/22/2018

Test Date . 03 / 03 /2018
Next Due Date 02 / 03 /2019

PAIL IND EQUIP COMPANY
Flat no A-2. Suvarnyug Coop Hsg
New D P Road, Aundh. Pune- 7.
Tel No 020 25886155
Mob 94220 88626

